OCTOBER 28TH, 2026

San Matías Pipeline

Technical Committee Meeting N°5

Documento: YPF-Público
CONFIDENTIAL

Agenda

1 > DEDICATED GAS PIPELINE UPDATE

- 1.1 > HSE Indicators
- 1.2 > Schedule
- 1.3 > Project's Key Milestones
- 1.4 > Project Progress

2 > PERMITS

3 > HELICOPTER SERVICE (Update)

1.1 > DEDICATED GAS PIPELINE UPDATE > HSE Indicators

Statistics through 30 Sep 2026 · CP + Pipeline · October highlights reported separately

TRICF Frequency

0


Cum. Aug–Sep · target 2.35
Through 30 Sep 2026

TVCR Frequency

0

Cum. Aug–Sep · target 0.79
Through 30 Sep 2026


Cumulative to 30 Sep 2026

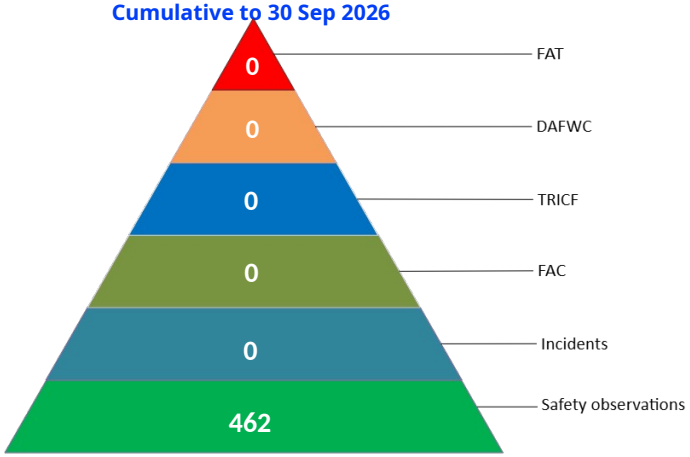


October KPIs · figures not provided

KPI	CP + Pipeline
DAFWCF (target 0)	Pending
TRICF (target 2.35 – 3)	Pending
TVCR (Target 0.79 – 2)	Pending
FAC (reporting)	Pending

TRICF · cases and frequency × 10^6 /HHT

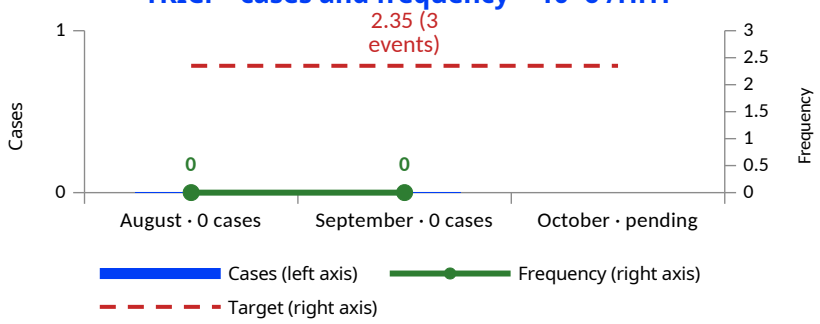

TVCR · cases and frequency × 10^6 /km travelled

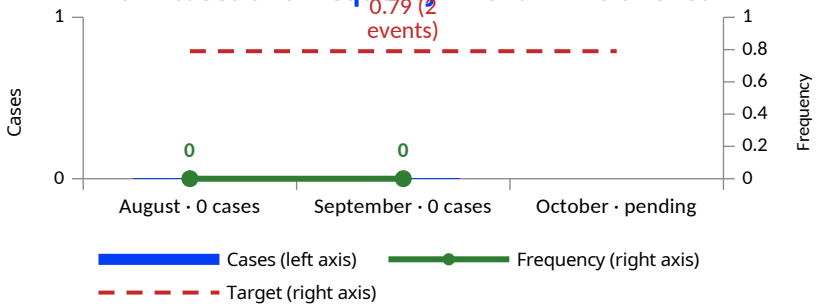


DAFWCF: lost-time cases × 10^6/ HHT
TRICF: recordable cases (FAT + DAFWC + MTC + RWC) × 10^6 / HHT
TVCR: Total Number of Work-Related Vehicle Accidents per Million Kilometres Travelled (× 10^6 / km travelled)


Documento: YPF-
Pública

CONFIDENTIAL


MANAGEMENT SAFETY WALKS

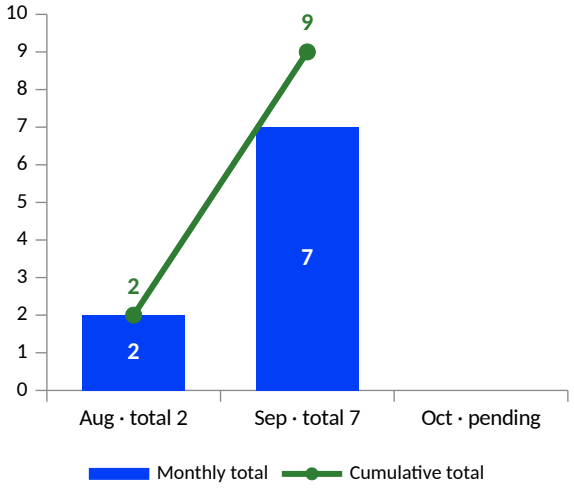


SAFETY CAMPAIGNS

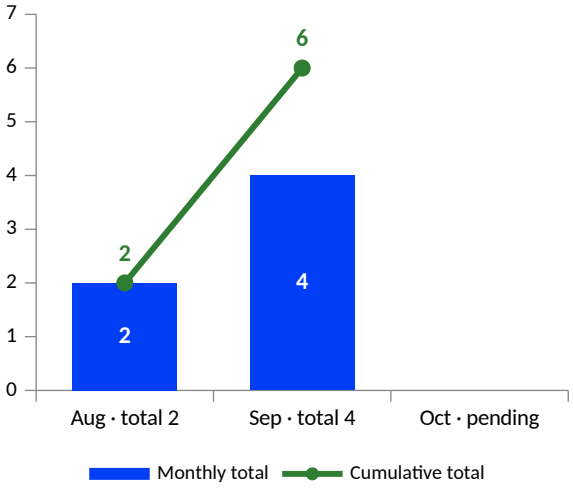


DRILLS · target 100%

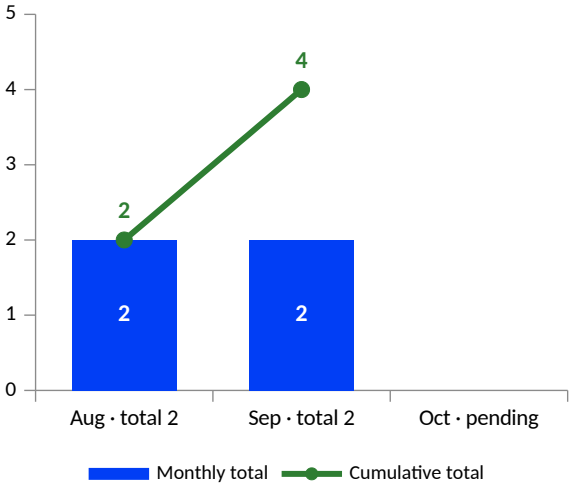

OBSERVATIONS (OCS)

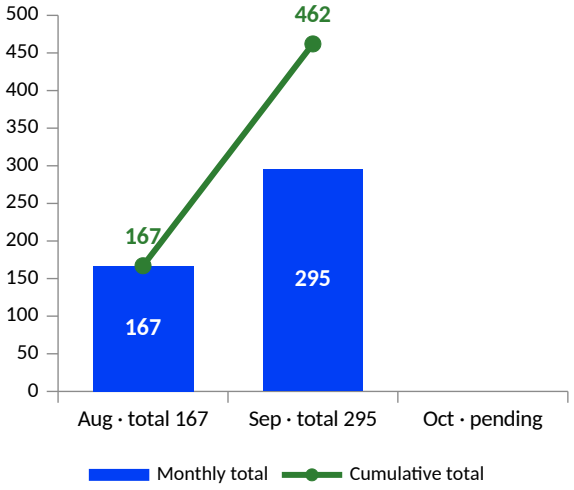

TRAINING HOURS (HHS)

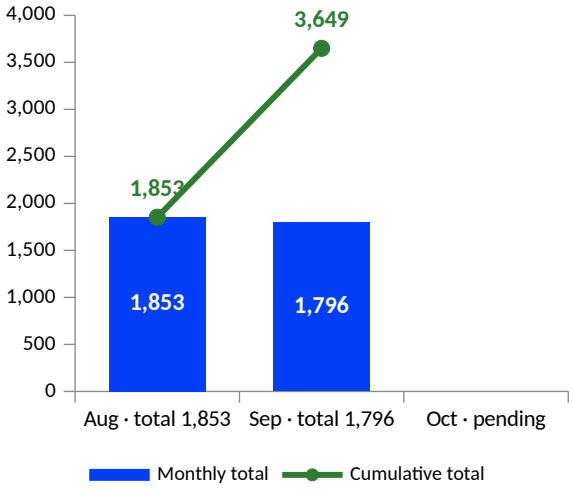

TRAINING · REPORTED VALUE

Training % vs HHT

2.87%

HHS / HHT · CP + Pipeline · target ≥ 1%

Documento: YPF-Pública

OCTOBER 2026 · PHOTOS & RELEVANT HIGHLIGHTS · cut-off 27 Oct

OCTOBER PHOTO 1
Pending actual photo

Date / location / activity: pending confirmation

OCTOBER PHOTO 2
Pending actual photo

Date / location / activity: pending confirmation

SAFETY — RELEVANT OCTOBER TOPICS


[Safety highlights and photos pending]
Confirmed development · relevance · next step

Documento: YPF-
Pública

CONFIDENTIAL

Statistics through 30 September 2026 · values unchanged

TOTAL WASTE GENERATION (kg/month)

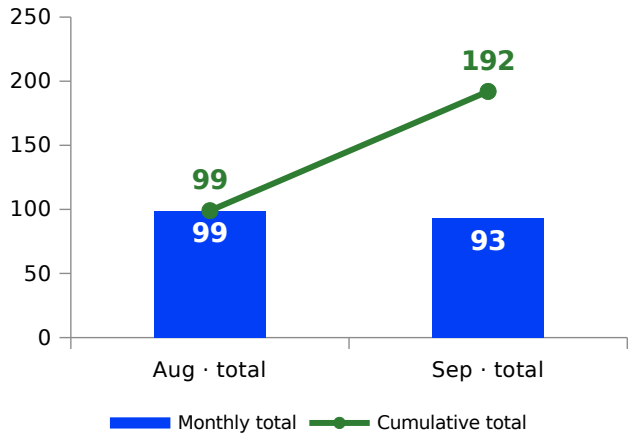


% Waste recovery

0%

% Waste final disposal / incinerated

100%

FRESHWATER CONSUMPTION (m³/month)

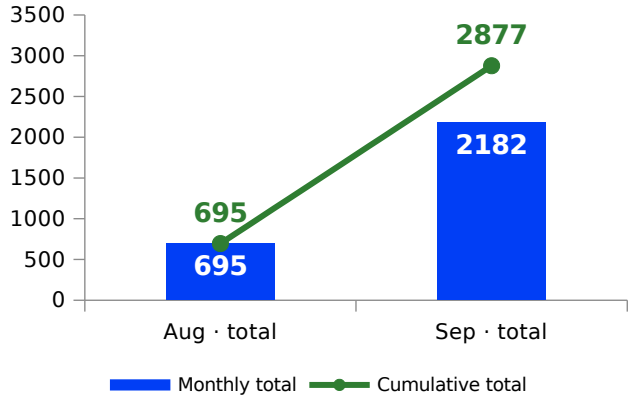

Documento: YPF-Público

OCTOBER 2026 · RELEVANT ENVIRONMENTAL TOPICS · reported 26 Oct

ALLEN COMPRESSOR PLANT — EIA ADDENDUM APPROVED

“Allen Compressor Plant Update” addendum approved on 21 October 2026 (Resolution 962/2026).

The decision on the cold vent stack (“Stack Frío”) remains pending. SMP must submit a comparative analysis of flaring and cold venting to the competent authority for discussion.

NEUQUÉN SECTION — WATER PERMIT PENDING

The response to comments on the Water Risk Study and its submission to SSRH remain pending, in coordination with Serman.

Purpose: advance the water permit application for the Neuquén section.

Statistical indicators remain as supplied, through 30 September 2026.

Documento: YPF-Público

CONFIDENTIAL

- **Background:**
  - **Vaca Muerta upstream major companies** (including PAE, YPF & Pampa) have a contract with MODENA for the provision of its services which consists of having a helicopter available for use in the event of a medical emergency.
  - **Vista** holds and manages a contract with MODENA covering aeromedical evacuation services for operators in Neuquén.
  - **VMOS** has a contract in force with MODENA for such services. The service originated as an ad hoc decision by YPF following an Emergency Response Risk Analysis.

- **Geographic Dispersion**
  - **SMP** pipeline route extends over 473 km along 2 provinces with sections located far away from high-complexity medical centres → Ground transportation may compromise the critical response time window during an emergency.

- **Labour Context**
  - Impact of the VMOS precedent in the event of an accident requiring this service
  - UOCRA agreement does not “explicitly” require this service for VMOS or SMP.

- **Actual Use, No Saturation**
  - Existing regional contracts (Neuquén and VMOS) recorded 40 to 50 emergencies over 3 years (approximately 1 to 2 per month), indicating there is operational capacity to include the SMP route.

- **Proposal to be discussed with Shareholders:**
  - Given the project’s extensive geographical footprint which includes remote areas with limited or no access to adequate medical infrastructure, it is recommended to have a helicopter available for emergency medical evacuation, particularly for incidents requiring medium- or high-complexity medical care.

Documento: YPF-Pública

Progress to date (cut-off Oct 27)

[Pending · YPF to provide status, milestones reached and dates]

Company auditing the service

[Pending · YPF to name the company that audits the service]

Option to add SESA

[Pending · YPF to confirm whether SESA can be added to the service]

Documento: YPF-Pública
