OCTOBER 28TH, 2026

San Matías Pipeline

Technical Committee Meeting N°5

Agenda

1 > DEDICATED GAS PIPELINE UPDATE

- 1.1 > HSE Indicators
- 1.2 > Safety Highlights
- 1.3 > Updates & Photo Log

2 > PERMITS

- 2.0 > Environmental Update

CONFIDENTIAL

TRICF Frequency

0


Cum. Aug–Sep · target 2.35

TVCR Frequency

0

Cum. Aug–Sep · target 0.79


Cumulative to 30 Sep 2026

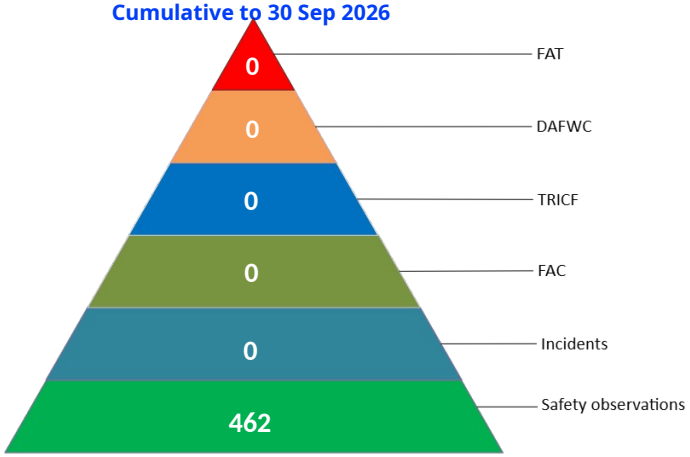


Other KPIs · September 2026

KPI	CP + Pipeline
DAFWCF (target 0)	0
TRICF (target 2.35 – 3)	0
TVCR (Target 0.79 – 2)	0
FAC (reporting)	0

TRICF · cases and frequency × 10^6 /HHT

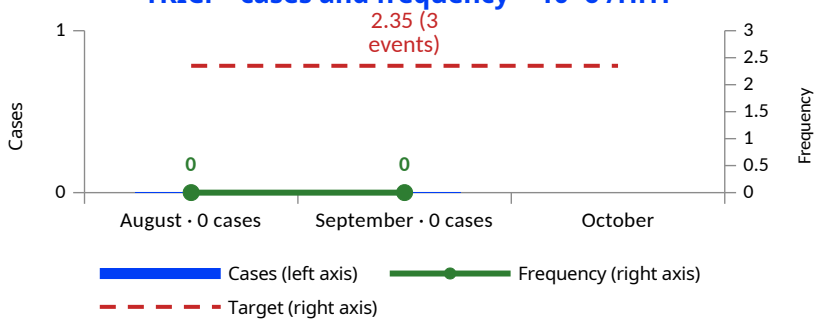

TVCR · cases and frequency × 10^6 /km travelled

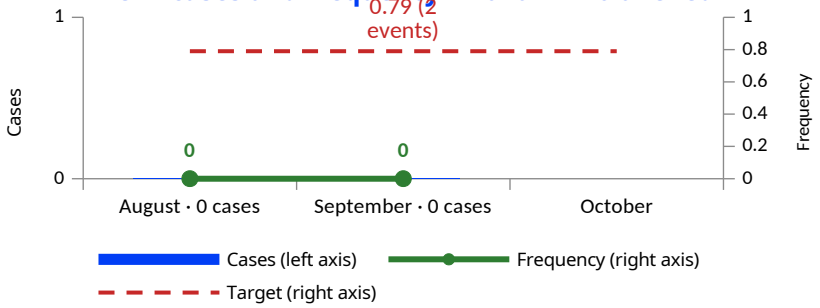


DAFWCF: lost-time cases × 10^6/ HHT
TRICF: recordable cases (FAT + DAFWC + MTC + RWC) × 10^6 / HHT
TVCR: Total Number of Work-Related Vehicle Accidents per Million Kilometres Travelled (× 10^6 / km travelled)


Documento: YPF-Pública

CONFIDENTIAL


MANAGEMENT SAFETY WALKS

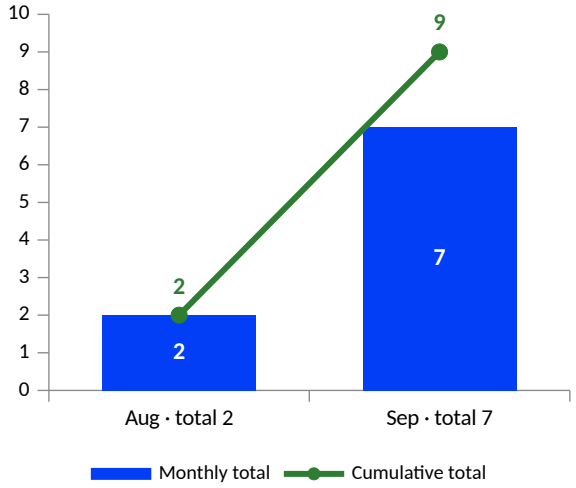


SAFETY CAMPAIGNS

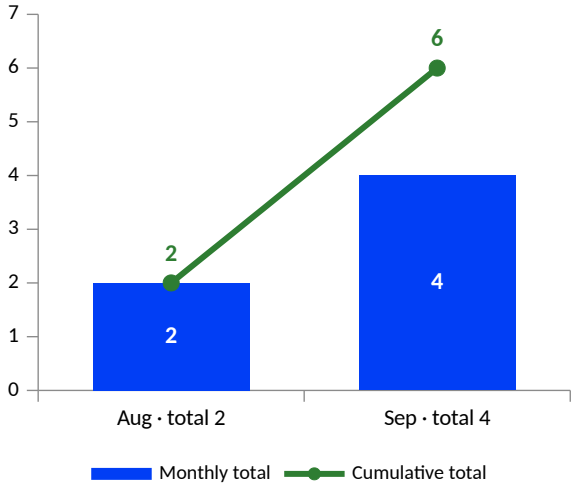


DRILLS · target 100%

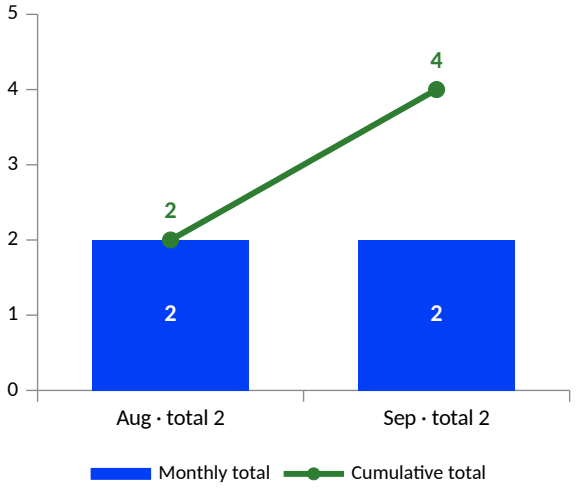

OBSERVATIONS (OCS)

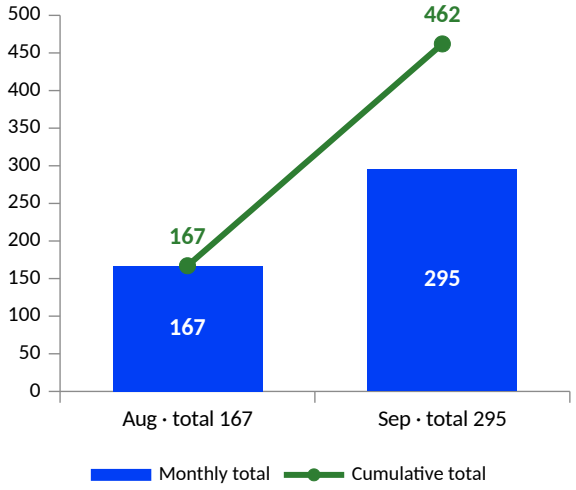

TRAINING HOURS (HHS)

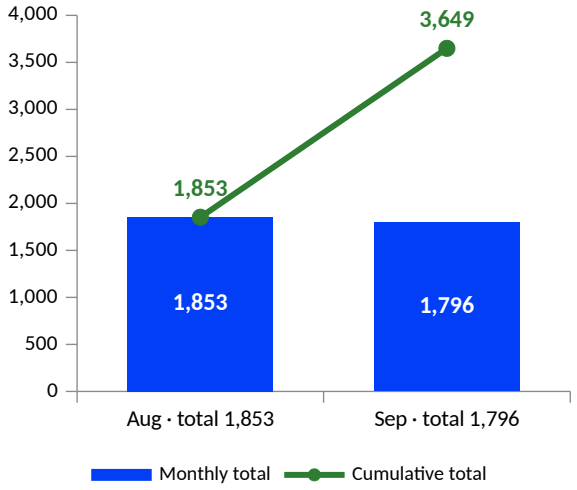

TRAINING · REPORTED VALUE

Training % vs HHT

2.87%

HHS / HHT · CP + Pipeline · target ≥ 1%

Documento: YPF-Pública

OCTOBER 2026 · GENERAL HSE HIGHLIGHTS · cut-off 27 Oct



RESCUE EQUIPMENT

All confined space rescue equipment was received on site.



EQUIPMENT TRAINING

Training on the use of the confined space rescue equipment was completed.



MANAGEMENT SAFETY WALKS

100% of the management safety walks scheduled up to the reporting cut-off were completed.

Documento: YPF-Pública

September 2026 · 2 photos per area: Compressor Plant, Pipeline (right-of-way) and Pipeline · SAE Port

COMPRESSOR PLANT



Compressor Plant site (1)



Compressor Plant site (2)

PIPELINE



Pre-trenching works



Pre-start safety talk before pipe unloading and stringing

PIPELINE · SAE PORT



Receiving pipe from the vessel · SAE Port



Loading onto transport at the laydown yard · SAE Port

OCTOBER 2026 · ENVIRONMENTAL PERMITS UPDATE

NEUQUÉN SECTION | WATER PERMIT

The response to comments on the Water Risk Study and submission to SSRH remain pending, in coordination with Serman, to advance the water permit application.

ALLEN COMPRESSOR PLANT | ENVIRONMENTAL ADDENDUM

The plant upgrade addendum has been approved. A decision on the cold vent stack (“Stack Frío”) remains pending. SMP must submit a comparative analysis of flaring and cold venting to the competent authority.

Documento: YPF-
Pública

The End
